CIVIL QUALITY CONSULTANTS AND ENGINEERS

PROJECT PLANNING/SCHEDULE

Client Name:

Project Name:

Project Start Date:

Project End Date:

Project Length in Days:

S. No	Assignment	Unit	Avg Qnty	Start Date	End Date	No. of Working Days
1	Earth work excavation for foundation of substation type I vehicle yard (service bay, transformer bay, control room, store, fencing and enclosure specifications, including setting out, preserving, shoring, working and bracing, removal of stumps and other obstruction matter, dressing of sides and bottom, filling back the excavated earth to the extent required and ramming / tamping the remaining earth upto 1.00km lead including cost of labour, material and OEM etc., complete as per specifications complete as per the direction of the Engineer in charge	Cum	400.00	6-Mar-23	19-Mar-23	10
2	Earth work excavation for foundation of substation type I vehicle yard (control room, store, fencing and enclosure specifications, including setting out, preserving, shoring, working and bracing, removal of stumps and other obstruction matter, dressing of sides and bottom, filling back the excavated earth to the extent required and ramming / tamping the remaining earth upto 1.00km lead including cost of labour, material and OEM etc., complete as per specifications complete as per the direction of the Engineer in charge	Cum	61.79	6-Mar-23	20-Mar-23	12
3	Earthwork excavation for foundation of buildings, culverts, water supply, sewerage, sanitary lines and electrical conduits either in pits or in trenches 1.5m and above in width, in ordinary soil not exceeding 3.0 m in depth including shoring the bottom and sides of pits and trenches, shifting the excavated soil beyond 1.5m from edges of excavation with lead upto 50 m, after breaking of clods complete, as per specifications, complete as per the direction of the Engineer in charge	Cum	347.36	6-Mar-23	21-Mar-23	15
4	Earthwork excavation for foundation of buildings, culverts, water supply, sewerage, sanitary lines and electrical conduits either in pits or in trenches 1.5m and above in width, in ordinary soil not exceeding 3.0 m in depth including shoring the bottom and sides of pits and trenches, shifting the excavated soil beyond 1.5m from edges of excavation with lead upto 50 m, after breaking of clods complete, as per specifications, complete as per the direction of the Engineer in charge	Cum	23.73	6-Mar-23	28-Mar-23	18
5	Providing and layering chemical solutions like Environmental Dust Suppressant Tetrasonic, including maintenance (chemical barrier works and erosion control of the stacks, soils, trenches, basement excavations, top surface of the plinth, filling, premises of wall and floor,using the mineral properties of leading/expansion constituents like top surface of consolidated earth etc which serve as a no loss/compounding of pores and residual soils, chloroprophene consolidation compositions of 20% concentration,including cost of chemical,labour,tools & water + one personal communication, labour, OEM, all requirements, complete as per specifications,(Work area of the building + ground floor only shall be measured) complete as per the direction of the Engineer in charge	Sqm	1,000.00	6-Mar-23	11-Mar-23	5
6	Construction of embankment with approved material (sand/ Murram) work all lifts and leads, transporting in any, spreading, grading to required slope and compacting to meet requirements Table 300.2 complete as per specifications, including cost of ground / structure, watering charges & compaction by vibratory roller to 95% of proctors density complete as per the direction of the Engineer in charge	Cum	147.30	8-Mar-23	23-Mar-23	11
7	Providing and laying in position Plain Cement Concrete of Mix 11:8 with Ordinary OPC cement @ 280kgs, with 40mm & down size graded granite metal coarse aggregates @ 0.80 cum & fine aggregates @ 0.57 cum machine mixed, machine mixed, concrete laid in layers not exceeding 15cms, thick well compacted, on foundations, including cost of all materials, labour, OEM of machinery, curing complete as per specifications complete as per the directions of the Engineer in charge	Cum	174.30	20-Mar-23	25-Mar-23	7
8	Providing and laying in position Plain Cement Concrete of mix 1:3:6 with Ordinary OPC cement @ 240kgs, with 20mm & down size graded granite metal coarse aggregates @ 1.870 cum & fine aggregates @ 0.53 cum machine mixed, machine mixed, concrete laid in layers not exceeding 15cms, thick well compacted, on foundations, plinth and Cills including cost of all materials, labour, OEM of machinery, curing complete as per specifications complete as per the direction of the Engineer in charge	Cum	340.78	26-Mar-23	5-Apr-23	10
9	Providing and laying in position plain concrete of nominal mix 1:3:6 Ordinary using 40mm and down size graded granite metal machine mixed, concrete laid in layers not exceeding 15 cms thick, well compacted, on foundations and plinth, including cost of all materials, labour, OEM machinery, curing complete as per specifications, complete as per the direction of the Engineers in charge.	Cum	3.75	3-Apr-23	29-Apr-23	19
10	Drawing cast-in-place vertical R.C.C. 300mm dia. piles with OPC cement @ 280kgs/cum, HYM @ 360 kgs, CASING PIPE 3.60 M MS with 20mm and down size graded granite metal coarse aggregates @ 0.80 cum and fine aggregates @ 0.46 cum, well, superplasticizer @ 3 ltr conforming to IS 9103:99 Reinforced 2000 including reinforcement as per drawings including cost of all materials, labour, OEM of machineries complete as per specifications, complete as per the direction of the Engineer in charge	Sqm	1312.80	26-Mar-23	30-Mar-23	10

Scanned by TapScanner

Sl. No	Assignment	Unit	Rate/ Cft/Sq	Start Date	End Date	No. of Working Days
11			54.40	20-Jul-21	1-Oct-21	53
12			7.40	30-Jul-21	23-Sep-21	5
13			5.55.00	25-Jul-21	13-Sep-21	18
14			81.76	14-Jul-21	29-Oct-21	53
15			41.00	30-Jul-21	9-Aug-21	10
16			55.93	1-Aug-21	11-Aug-21	10
17			90.00	1-Aug-21	13-Sep-21	40
18			51.00	13-Sep-21	25-Sep-21	10
19			414.00	16-Jul-21	23-Jul-21	5
20			1395.54	16-Jul-21	21-Jul-21	5
21			13.27	16-Jul-21	11-Aug-21	15
22			107.08	16-Jul-21	29-Jul-21	10

Scanned by TapScanner

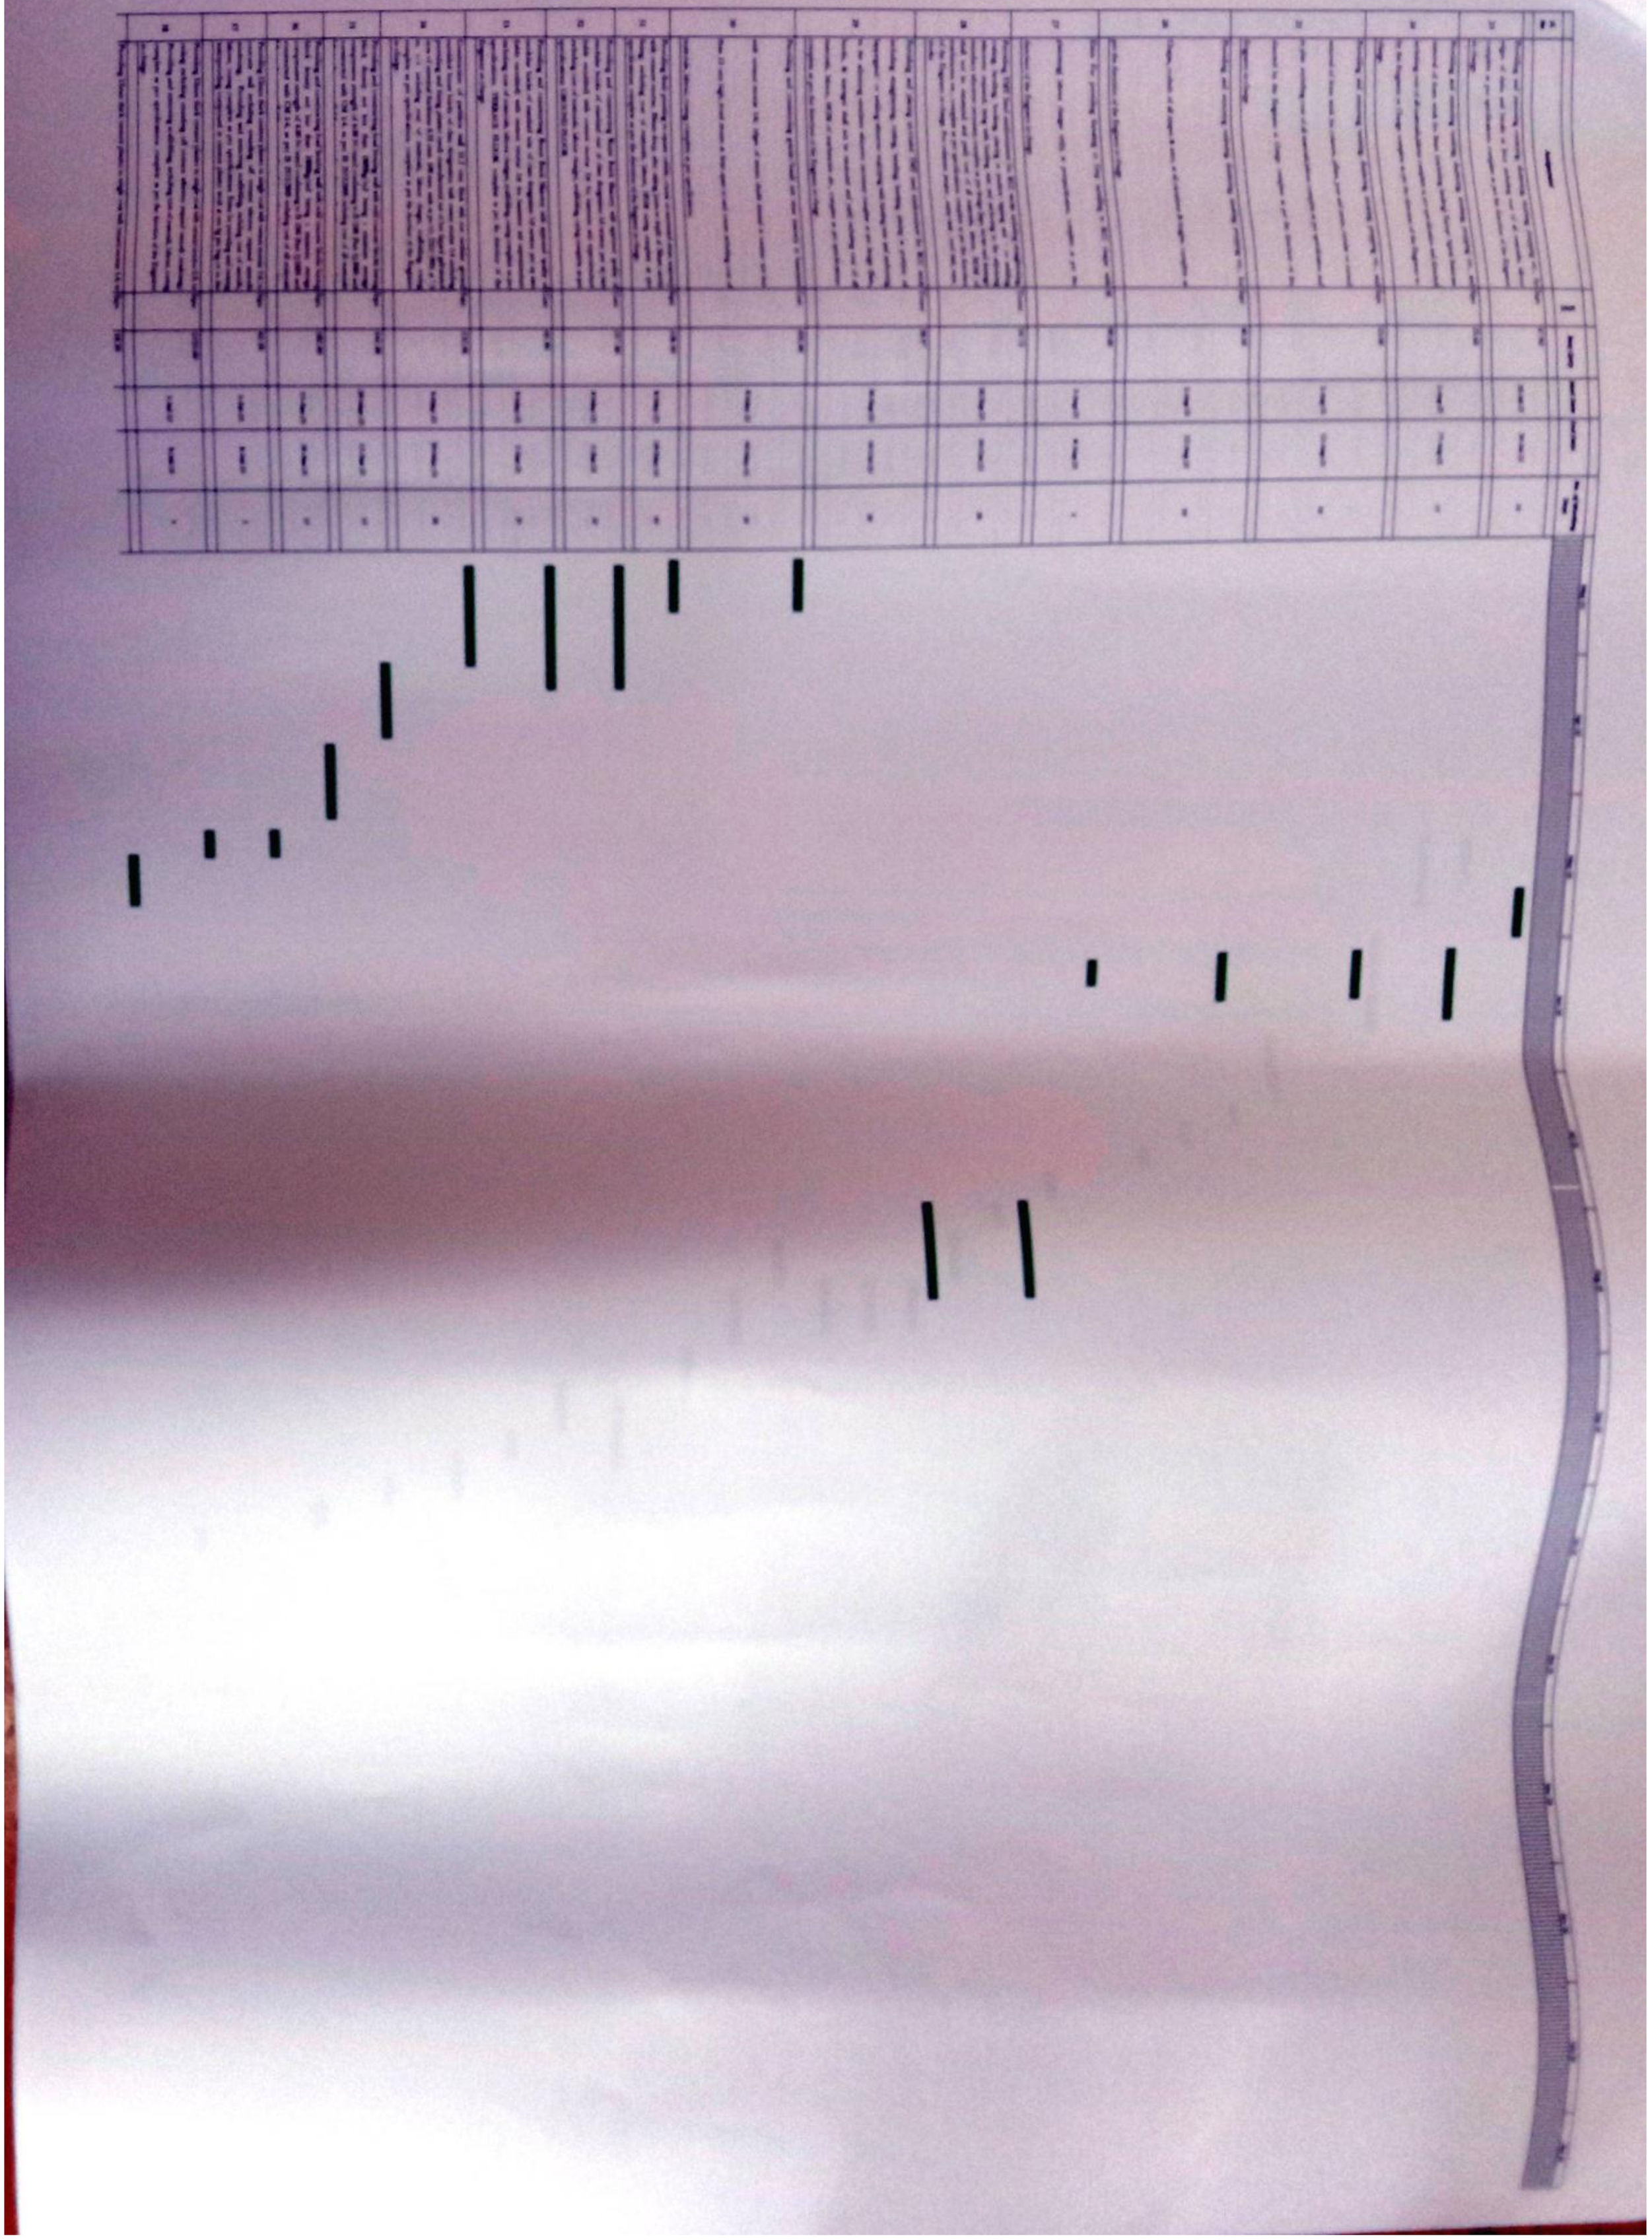

Scanned by TapScanner

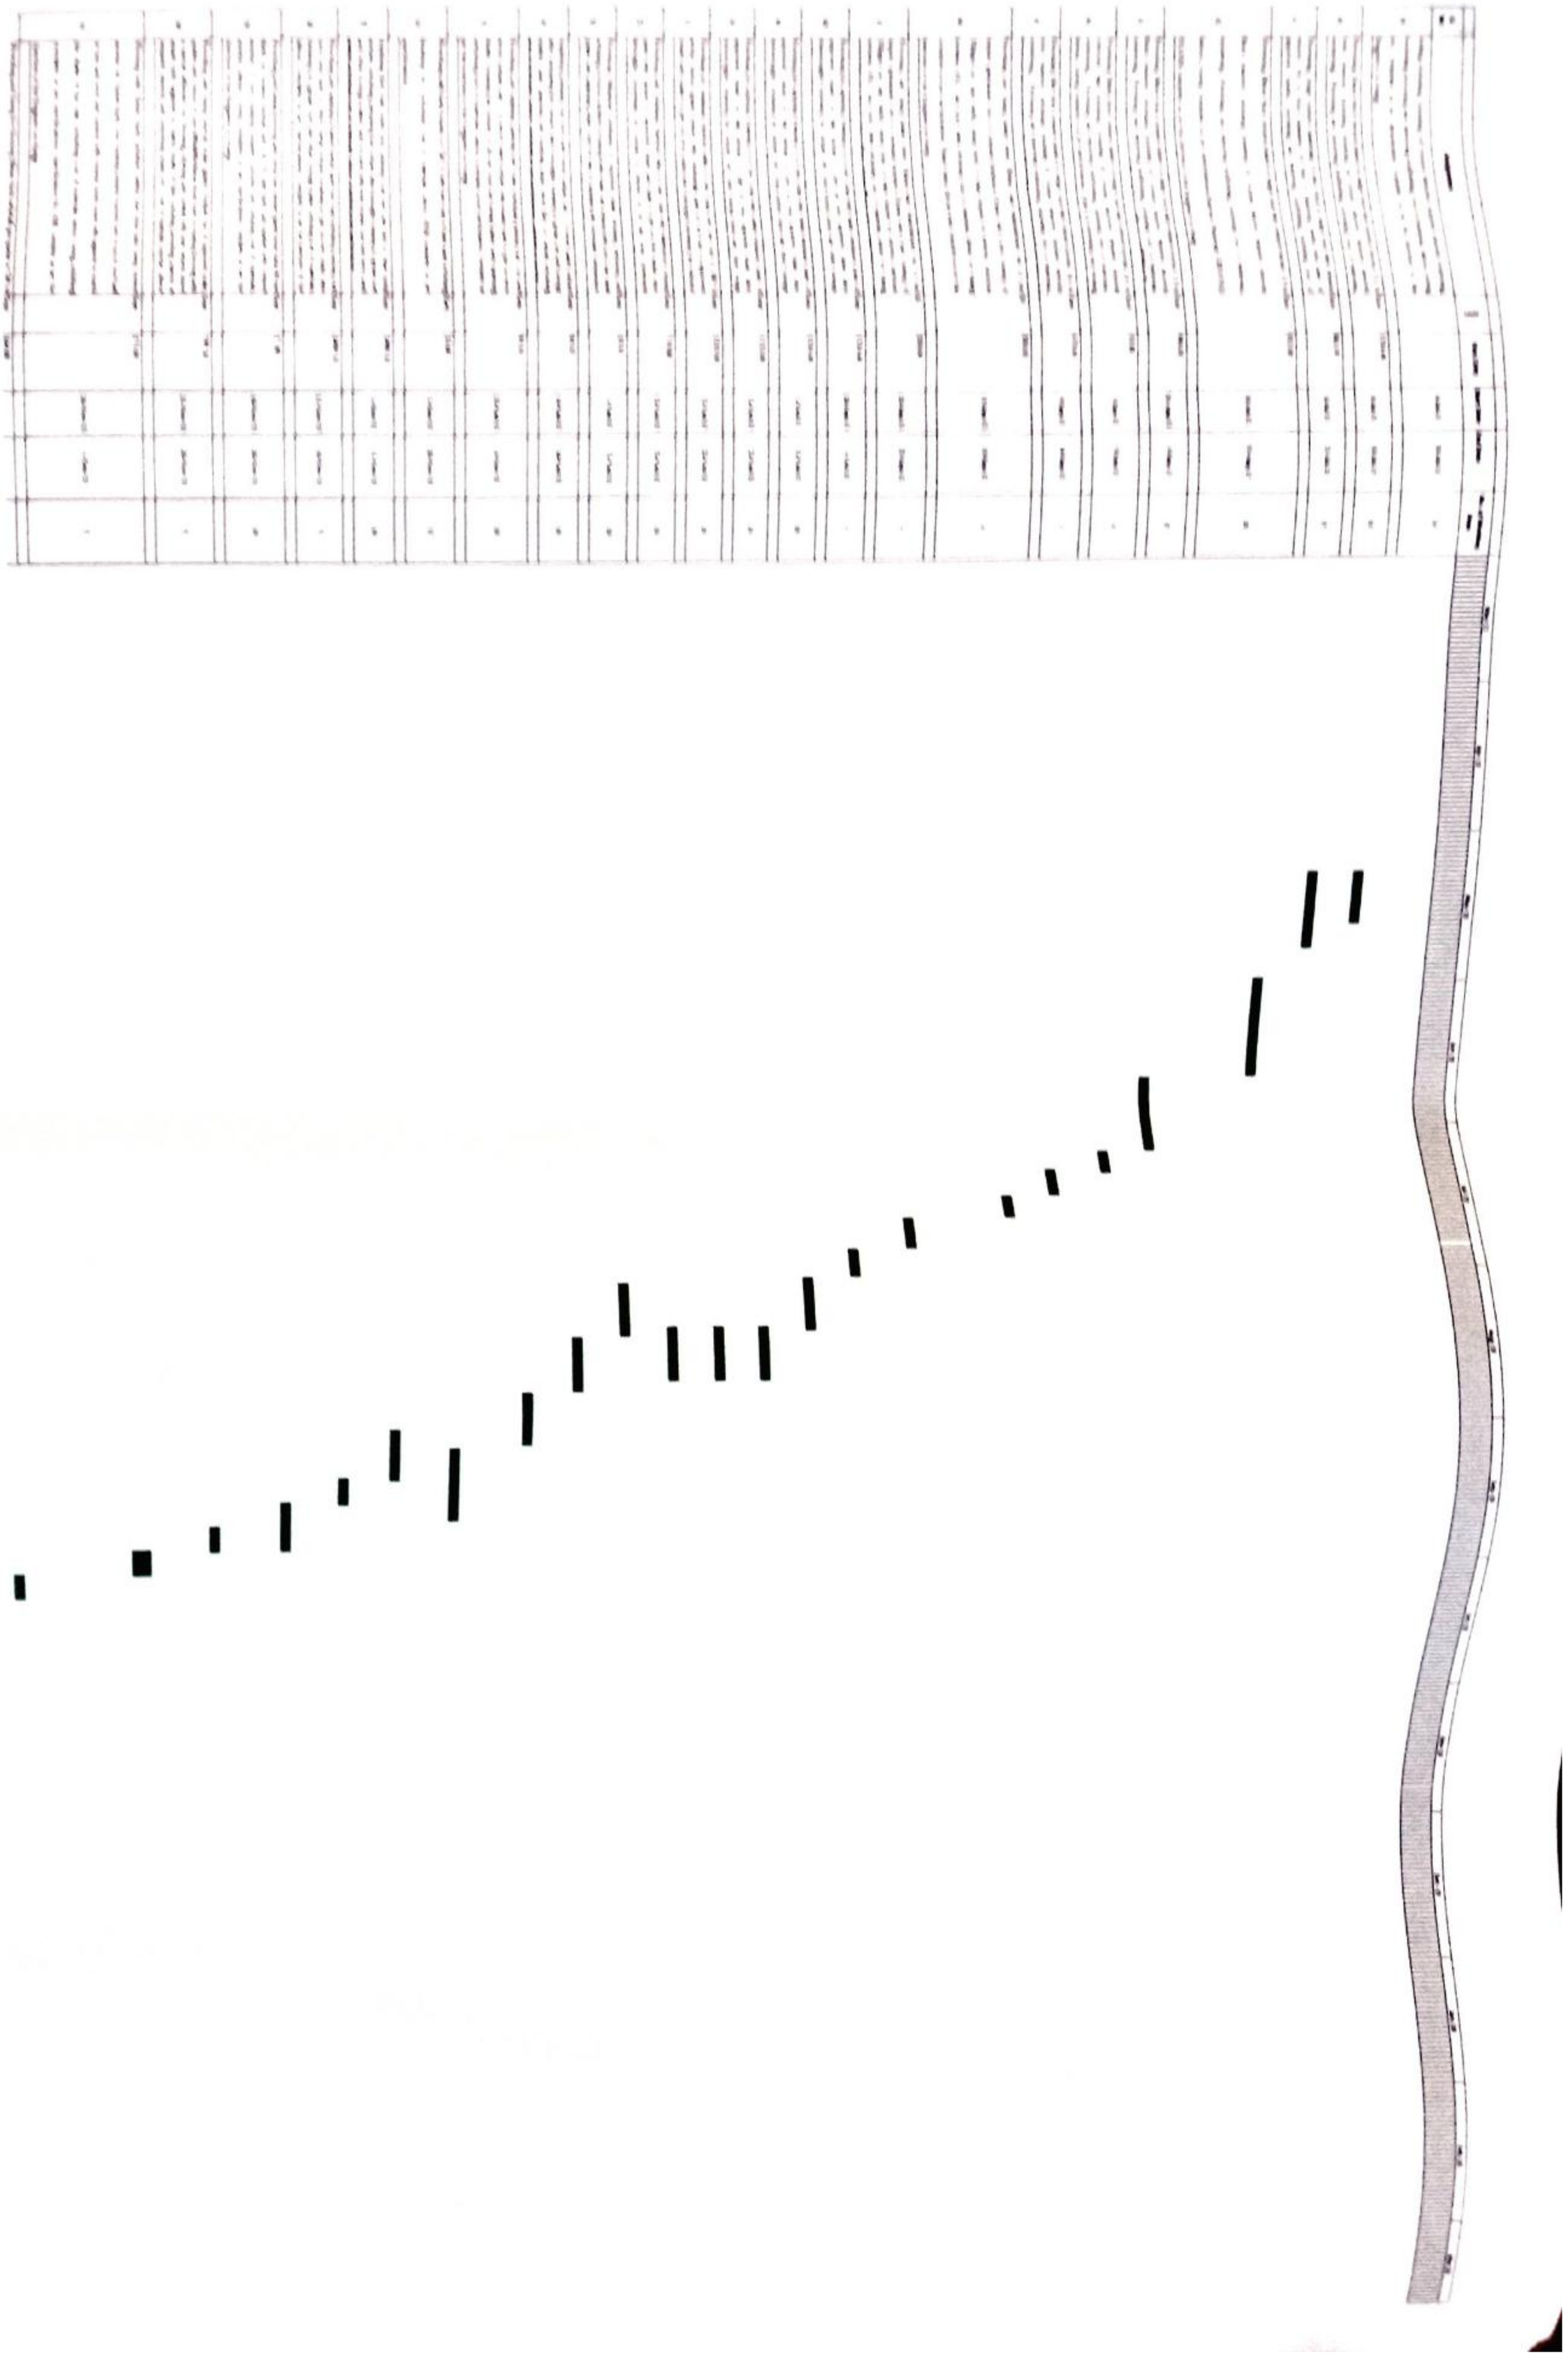

Scanned by TapScanner

S/No	Assignment	Unit	Req'd Quty	Start Date	End Date	No. of Working Days
62	[illegible]			1-Dec-21	6-Dec-21	5
63	[illegible]		13.50	1-Dec-21	9-Dec-21	5
64	[illegible]		13.00	30-Nov-21	4-Aug-21	5
65	[illegible]	M	24.30	9-Sep-21	19-Sep-21	10
66	[illegible]		156.00	20-Sep-21	30-Sep-21	10
67	[illegible]		475.70	30-Sep-21	5-Oct-21	5
68	[illegible]		807.20	5-Oct-21	15-Oct-21	10
69	[illegible]		6.15	5-Oct-21	15-Oct-21	10
70	[illegible]		0.54	5-Oct-21	15-Oct-21	10
71	[illegible]		5.10	15-Oct-21	25-Oct-21	10
	[illegible]		45.00			

Scanned by TapScanner

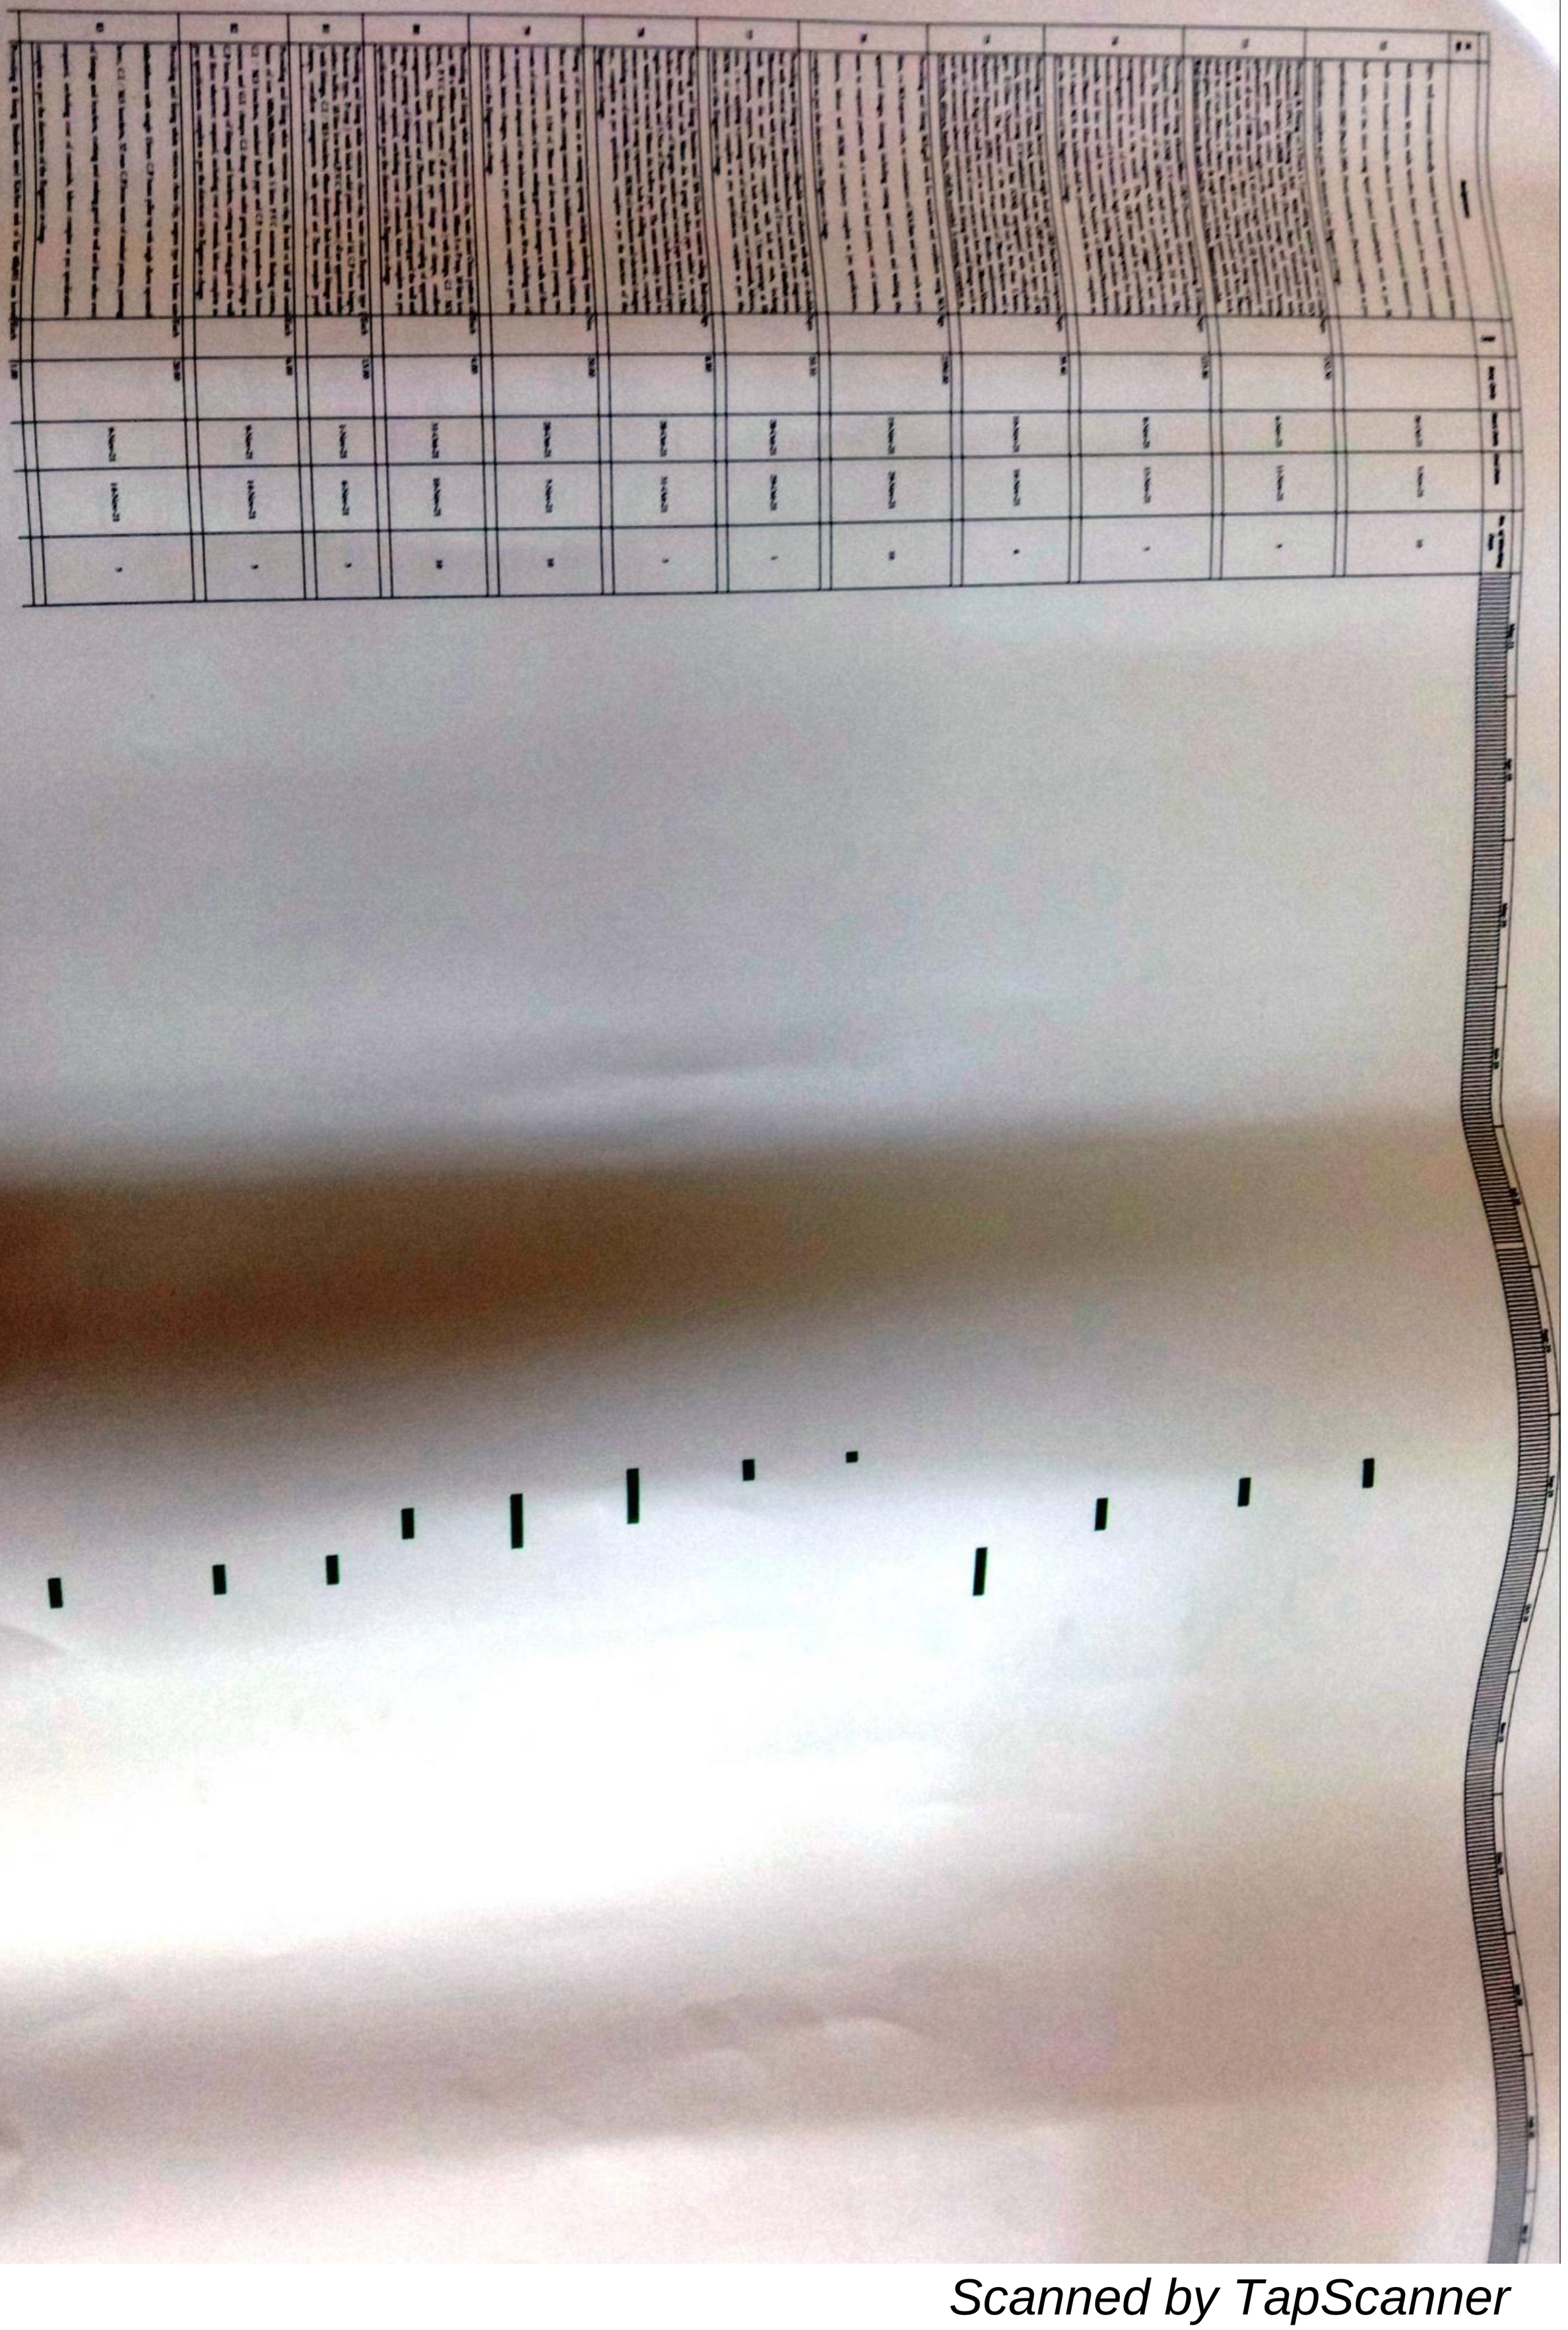

Scanned by TapScanner

Sl. No.	Assignment	Unit	Req Qnty	Start Date	End Date	No. of Working Days
84	Depth 600 mm with clear inner, MS - 12 bracket, bamboo steel plug 40 mm, forming of Fittings and brackets, cutting and making good the wall and floor wherever required, including cost of materials, labour complete as per specifications, complete as per the direction of the Engineer in-charge			9-Nov-21	14-Nov-21	5
85	Providing and fixing 600x600mm Bronzed edge mirror of superior glass with 6 mm thick steel framed backing and fixed wooden cleat with CP screws, fenders, including cost of materials, labour complete as per specifications, complete as per the direction of the Engineers in-charge	Each	20.00	10-Nov-21	15-Nov-21	5
86	Providing and fixing C P brass towel rail 600 mm length 20 mm with C P bracket fixed to wooden cleat with CP brass screws, washers, including cost of materials, labour complete as per specifications, complete as per the direction of the Engineers in-charge	Each	8.00	26-Nov-21	10-Dec-21	10
87	Providing & fixing 12 Halsey top of approved make conforming to IS: specifications and construction of coarse in M 15 as per direction, complete as per the directions of the Engineer in-charge	Each	30.00	30-Nov-21	10-Dec-21	10
88	Providing and fixing CP Health faucet with flexible hose,CP Angle valve, wall flange, supporting hook with screws, fixing materials and washer to all sides of wall flange complete, complete as per the direction of the Engineer in-charge	Each	15.00	5-Dec-21	10-Dec-21	5
89	Providing and fixing in position C P soap dish with pair of fixing screws and fixing material complete, complete as per the direction of the Engineers in-charge	Each	20.00	5-Dec-21	10-Dec-21	5
90	Providing and fixing in position Brass bib cock of approved quality 20 mm nominal bore including cost of all materials, labour and HOM of equipments with all leads complete as per specifications, complete as per the direction of the Engineer in-charge	Each	30.00	6-Dec-21	7-Dec-21	2
91	Providing and fixing in position brass Stop cock of approved quality 20 mm nominal bore including cost of all materials, labour and HOM of equipments with all leads complete as per specifications, complete as per the direction of the Engineer in-charge	Each	10.00	6-Dec-21	7-Dec-21	2
92	Providing and fixing in on plasticised PVC Connection pipe with brass union 15 mm nominal bore 450 mm length of PVC connection including cost of all materials, labour and HOM of equipments with all leads complete as per specifications complete as per the direction of the Engineer in-charge	Each	75.00	6-Dec-21	8-Dec-21	3
93	Providing and fixing in position 25 mm nominal bore gate metal seat screw valve horizontal type of approved make including cost of all materials, labour and HOM of equipments with all leads complete as per specifications complete as per the direction of the Engineers in-charge	Each	2.00	8-Dec-21	11-Dec-21	3
94	Providing and fixing to wall, ceiling and floor , High density polyethylene pipes 6.00 kgf / sqcm working pressure 63 mm outside diameter with special flange, compression type fittings, wall clips, making good the wall, ceiling and floor including cost of all materials, labour and HOM of equipments with all	Each	20.00	13-Dec-21	18-Dec-21	5
95	Providing and fixing to wall, ceiling and floor , High density polyethylene pipes 6.00 kgf / sqcm working pressure 63 mm outside diameter with special flange, compression type fittings, wall clips, making good the wall, ceiling and floor including cost of all materials, labour and HOM of equipments with all leads complete as per specifications. b) 75 mm dia complete as per the	Each	30.00	21-Dec-21	23-Dec-21	2
96	Providing and fixing to wall, ceiling and floor , High density polyethylene pipes 6.00 kgf / sqcm working pressure 63 mm outside diameter with special flange, compression type fittings, wall clips, making good the wall, ceiling and floor including cost of all materials, labour and HOM of equipments with all leads complete as per specifications. c) 90 mm dia complete as per the direction of the Engineers in-charge	Each	30.00	9-Dec-21	11-Dec-21	2
97	Providing and fixing to wall, ceiling and floor , High density polyethylene pipes 6.00 kgf / sqcm working pressure 63 mm outside diameter with special flange, compression type fittings, wall clips, making good the wall, ceiling and floor including cost of all materials, labour and HOM of equipments with all leads complete as per specifications. d) 110 mm dia complete as per the direction of the Engineers in-charge	Each	30.00	11-Dec-21	13-Dec-21	2
98	Providing & Fixing in position heavy duty C P grating with frame of below mentioned sizes including painting and fixing material complete a) 75 mm dia complete as per the direction of the Engineer in-charge	Each	30.00	11-Dec-21	12-Dec-21	1
99	Providing and fixing to wall, ceiling and floor chlorinated poly vinyl chloride (CPVC) pipes conforming to IS 15778, having thermal stability for hot and cold water supply including all cpvc plain and bronze threaded fittings including	Each	30.00	9-Dec-21	10-Dec-21	2
100	Providing and fixing to wall, ceiling and floor chlorinated poly vinyl chloride (CPVC) pipes conforming to IS 15778, having thermal stability for hot and cold water supply including all cpvc plain and bronze threaded fittings including fixing the pipes with the clamps at 1.00 mtr spacing This includes joining of pipes fittings with one set of cpvc solvent cement and testing of joints complete (Internal works) (Concealed work including cutting chases and good the walls etc.) B)20mm dia pipe nominal OD pipes, complete as per the direction of the Engineers in-charge	Each	100.00	24-Dec-21	29-Dec-21	5
101	Providing and fixing in position brass gate valve with CI wheel of approved quality (screwed end) NB including cost of all materials, labour and HOM of equipments with all leads complete as per specifications, c) of 20mm dia,	Each	12.00	20-Sep-21	25-Sep-21	5
102	Providing and fixing in position brass gate valve with CI wheel of approved quality (screwed end) NB including cost of all materials, labour and HOM of equipments with, all leads complete as per specifications, b) of 25mm dia, complete as per the direction of the Engineers in-charge	Each	2.00	26-Sep-21	1-Oct-21	5

Scanned by TapScanner

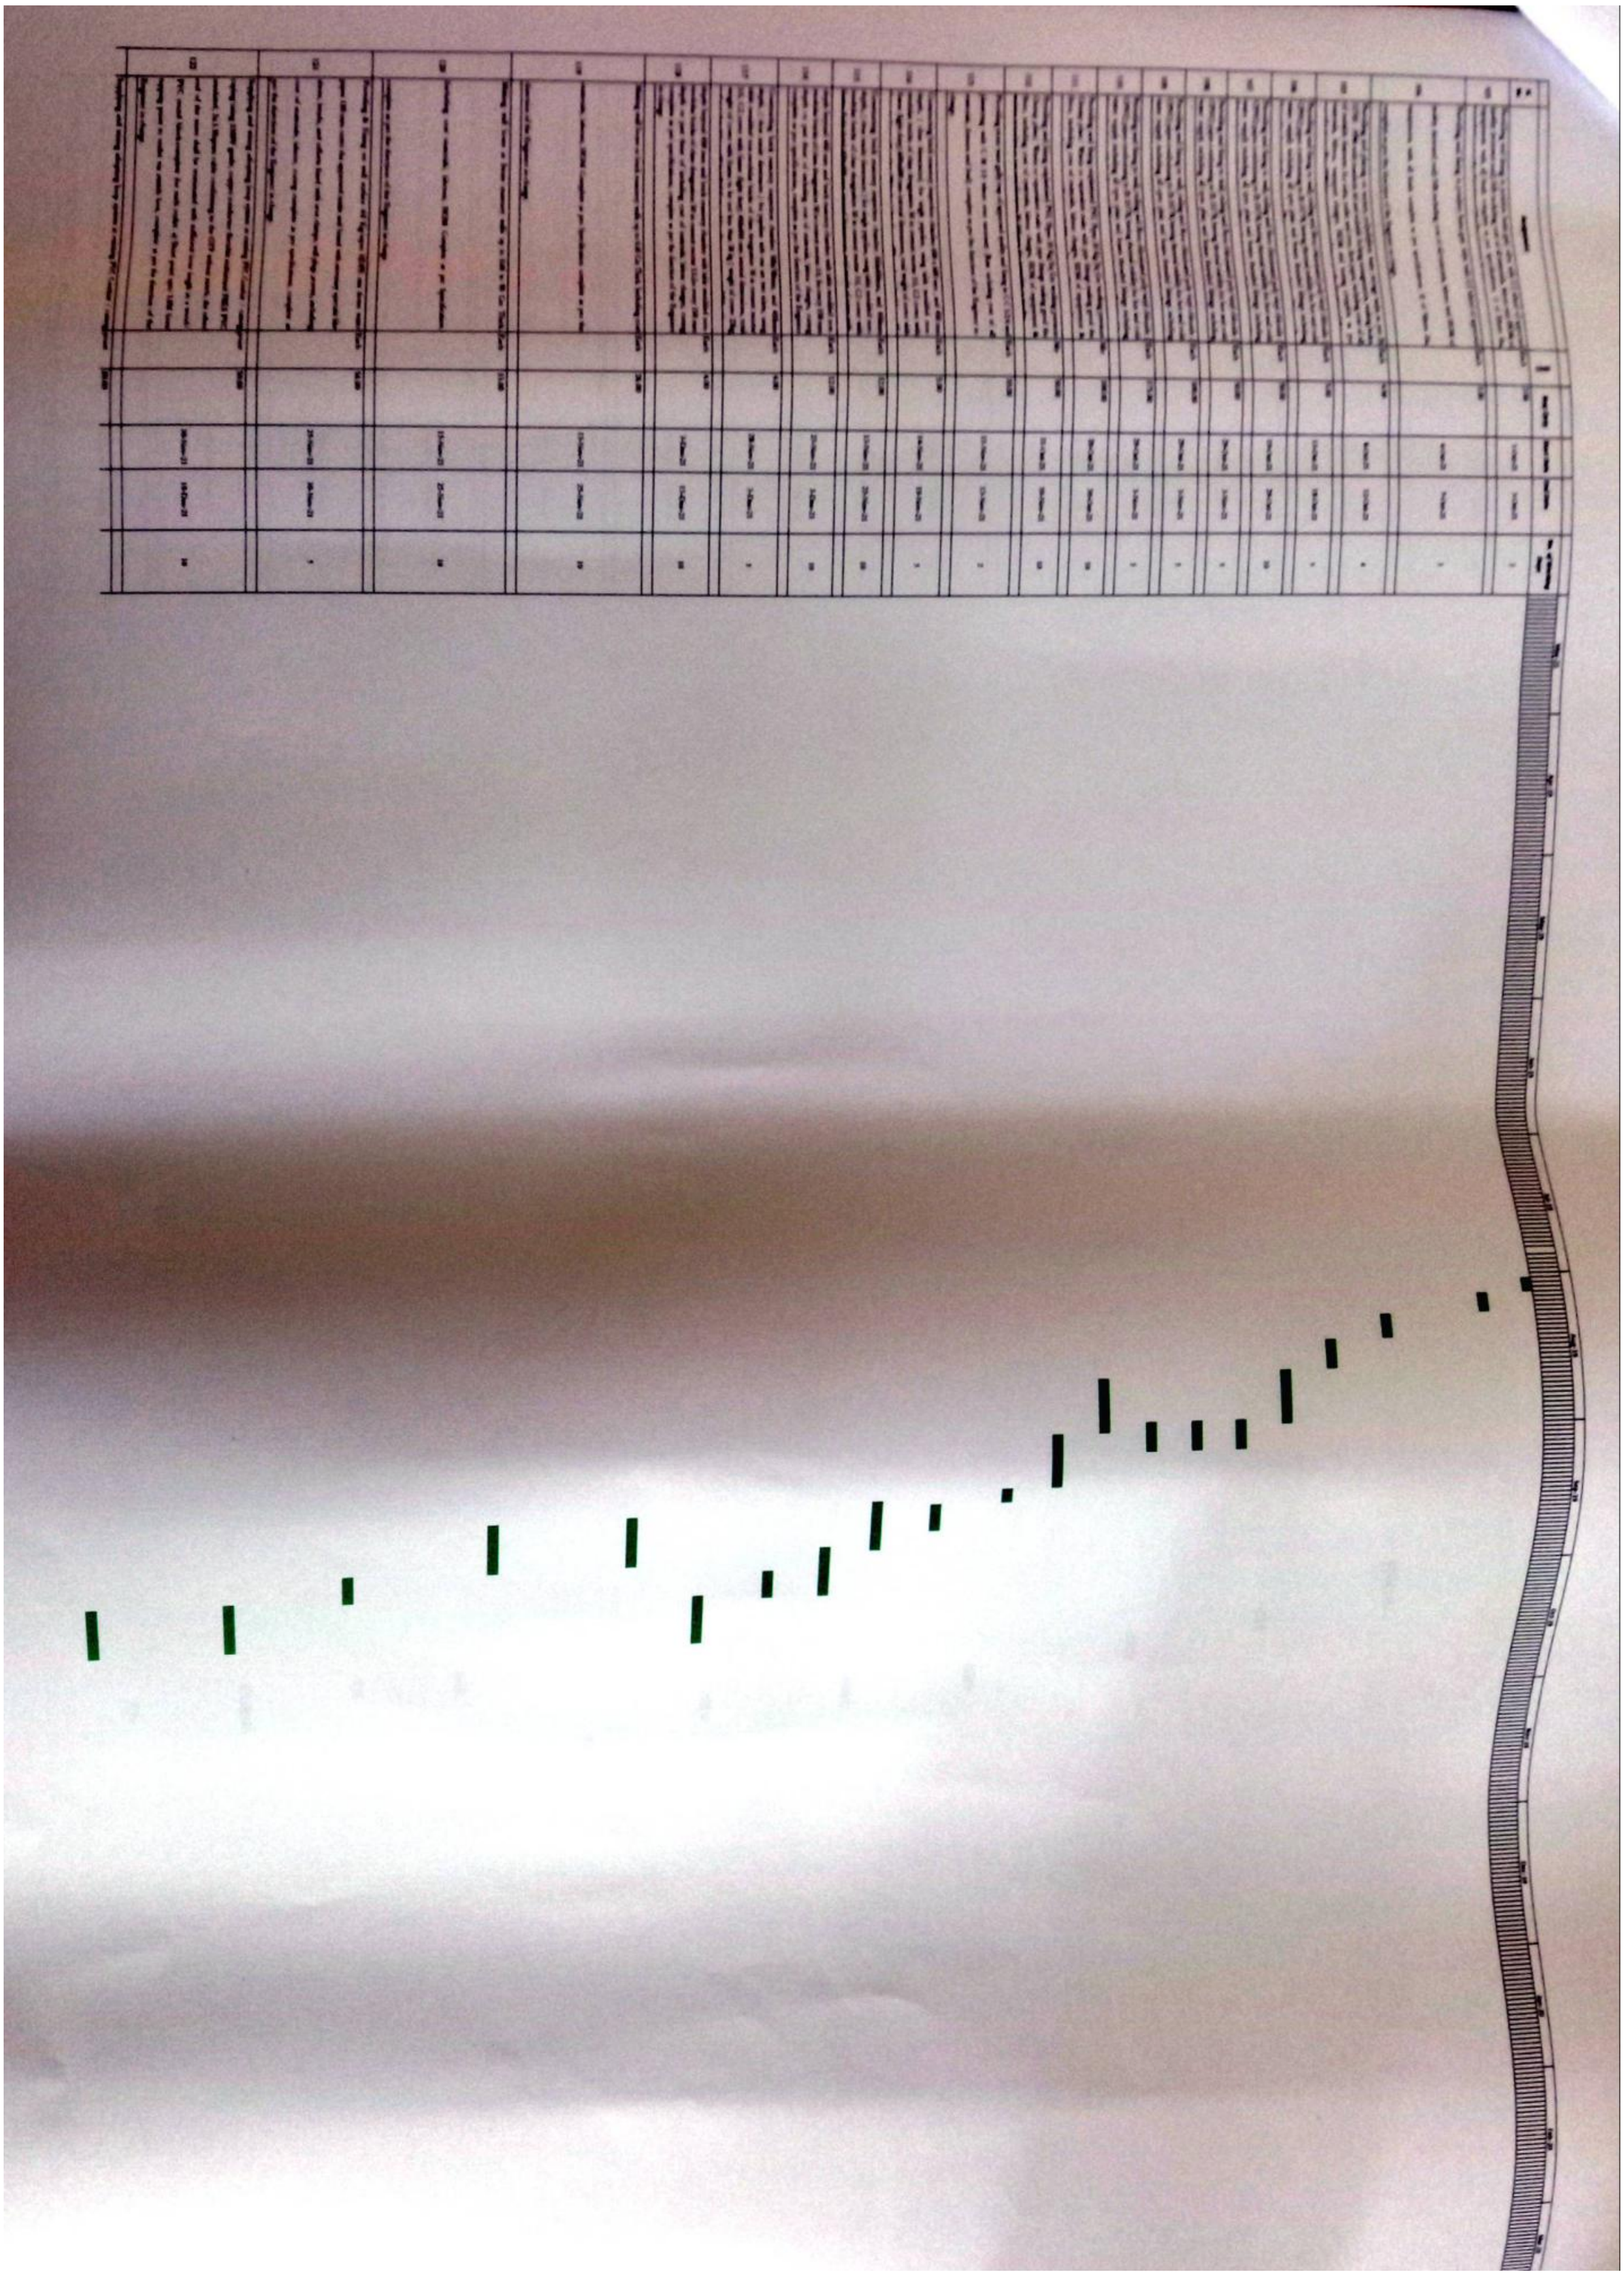

Scanned by TapScanner

Sl. No.	Assignment	Sl.	Anal Carry	Start Date	End Date	No. of Working Days
123	Supplying and fixing 110(V) grade, super resistance flexible reinforced FRLS PVC conduit, 2x1.5Sqmm cable conforming to the GTP without rewire, the entire assembly

Sl. No	Assignment	Unit	Req Qtty	Start Date	End Date	No. of Working Days
133	Supplying and fixing of modular switch socket engaged electronic tel/Data outlet in regulator/dimmer/telephone socket on existing modular switch plate as per IS 3854 and IS 1293 e.Design one Way, complete as per the direction of the Engineer-in-charge	Each	150.00	22-Dec-21	27-Dec-21	5
134	Supplying and fixing of modular switch socket engaged electronic tel/Data outlet in regulator/dimmer/telephone socket on existing modular switch plate as per IS 3854 and IS 1293 (a) 6Amps Two way complete as per the direction of the Engineer-in-charge	Each	6.00	30-Dec-21	4-Jan-22	5
135	Supplying and fixing of modular switch socket engaged electronic tel/Data outlet in regulator/dimmer/telephone socket on existing modular switch plate as per IS 3854 and IS 1293 (c) 6Amps Intermediate, complete as per the direction of the Engineer-in-charge	Each	45.00	30-Dec-21	4-Jan-22	5
136	Supplying and fixing of modular switch socket engaged electronic tel/Data outlet in regulator/dimmer/telephone socket on existing modular switch plate as per IS 3854 and IS 1293 d) 16Amps Heavy duty, complete as per the direction of the Engineer-in-charge	Each	30.00	30-Dec-21	4-Jan-22	5
137	Supplying and fixing of modular switch socket engaged electronic tel/Data outlet in regulator/dimmer/telephone socket on existing modular switch plate as per IS 3854 and IS 1293 e) 16Amps one way switch, complete as per the direction of the Engineer-in-charge	Each	2.00	31-Dec-21	5-Jan-22	5
138	Supplying and fixing of modular switch socket engaged electronic tel/Data outlet in regulator/dimmer/telephone socket on existing modular switch plate as per IS 3854 and IS 1293 f) 16Amps two way switch, complete as per the direction of the Engineer-in-charge	Each	6.00	14-Jan-22	19-Jan-22	5
139	Supplying and fixing of modular switch socket engaged electronic tel/Data outlet in regulator/dimmer/telephone socket on existing modular switch plate as per IS 3854 and IS 1293 g) 16Amps Intermediate switch, complete as per the direction of the Engineer-in-charge	Each	30.00	14-Jan-22	19-Jan-22	5
140	Supplying and fixing of modular switch socket engaged electronic tel/Data outlet in regulator/dimmer/telephone socket on existing modular switch plate as per IS 3854 and IS 1293 (i) 6Amps 3pin, complete as per the direction of the Engineer-in-charge	Each	2.00	14-Jan-22	19-Jan-22	5
141	Supplying and fixing of modular switch socket engaged electronic tel/Data outlet in regulator/dimmer/telephone socket on existing modular switch plate as per IS 3854 and IS 1293 g) 6 16Amps universal socket, complete as per the direction of the Engineer-in-charge	Each	30.00	14-Jan-22	19-Jan-22	5
142	Supplying and fixing of modular switch socket engaged electronic tel/Data outlet in regulator/dimmer/telephone socket on existing modular switch plate as per IS 3854 and IS 1293 h) TV /Telephone socket, complete as per the direction of the Engineer-in-charge	Each	6.00	19-Jan-22	24-Jan-22	5
143	Supply and fixing of 6Amps bell buzzer on existing switch board, complete as per the direction of the Engineer-in-charge	Each	2.00	1-Oct-21	6-Oct-21	5
144	Supplying following non heavy gauge PVC conduit pipe and following (work) Min conforming to IS 2509 with suitable size bends, Metal PVC/precision boxes, adhesive paste etc, and removing broken concreting the slab. The conduit should be laid in the reinforcement coils by using binding wires and unwanted ways of junction boxes and pipe ends should be covered using PVC end caps/screw on type with GI/MS/G.I Fish wire where ever necessary (i) 20mm dia	Min	800.00	6-Oct-21	11-Oct-21	5
145	Supplying following non heavy gauge PVC conduit pipe and following (work) Min conforming to IS 2509 with suitable size bends, Metal PVC/precision boxes, adhesive paste etc, and removing broken concreting the slab. The conduit should be laid in the reinforcement coils by using binding wires and unwanted	Min	300.00	6-Oct-21	11-Oct-21	5
146	Supplying following non heavy gauge PVC conduit pipe and following (work) Min conforming to IS 2509 with suitable size bends, Metal PVC/precision boxes, adhesive paste etc, and removing broken concreting the slab. The conduit should be laid in the reinforcement coils by using binding wires and unwanted ways of junction boxes and pipe ends should be covered using PVC end caps/screw on type with GI/MS/G.I Fish wire where ever necessary (i) 32mm dia 2.5mm thick, complete as per the directions of the Engineer-in-charge	Min	20.00	6-Oct-21	12-Oct-21	6
147	Supplying heavy gauge pvc conduit pipe ...dia mm thick with suitable size bends, metal junction boxes adhesive paste etc ,by gamon cutting on the wall and fixing by hearing U & J hooks and General plastering upto the wall surface and rem with 18 SWG GI fish wire throughout the conduit where	Min	900.00	12-Oct-21	22-Oct-21	10
148	Supplying heavy gauge pvc conduit pipe ...dia mm thick with suitable size bends, metal junction boxes adhesive paste etc ,by gamon cutting on the wall and fixing by hearing U & J hooks and General plastering upto the wall surface and rem with 18 SWG GI fish wire rem throughout the conduit where	Min	300.00	24-Oct-21	8-Nov-21	15
149	Wiring for lightning protect cortcut wiring rem of FRLS PVC insulated 1100v/M grade, multistrand Copper with low conductive resistance single core wire as specified IS 694/1990 & conforming to GTP of Group-A, 6) 1.5sqmm, complete as per the direction of the Engineer-in-charge	M	2880.00	11-Nov-21	26-Nov-21	15
150	Wiring for lightning protect cortcut wiring rem of FRLS PVC insulated 1100v/M grade, multistrand Copper with low conductive resistance single core wire as specified IS 694/1990 & conforming to GTP of Group-A, b) 2.5sqmm, complete as per the direction of the Engineer-in-charge	M	5000.00	13-Dec-21	23-Dec-21	10
	Wiring for lightning protect cortcut wiring rem of FRLS PVC insulated 1100v/M	M	1300.00			

Scanned by TapScanner

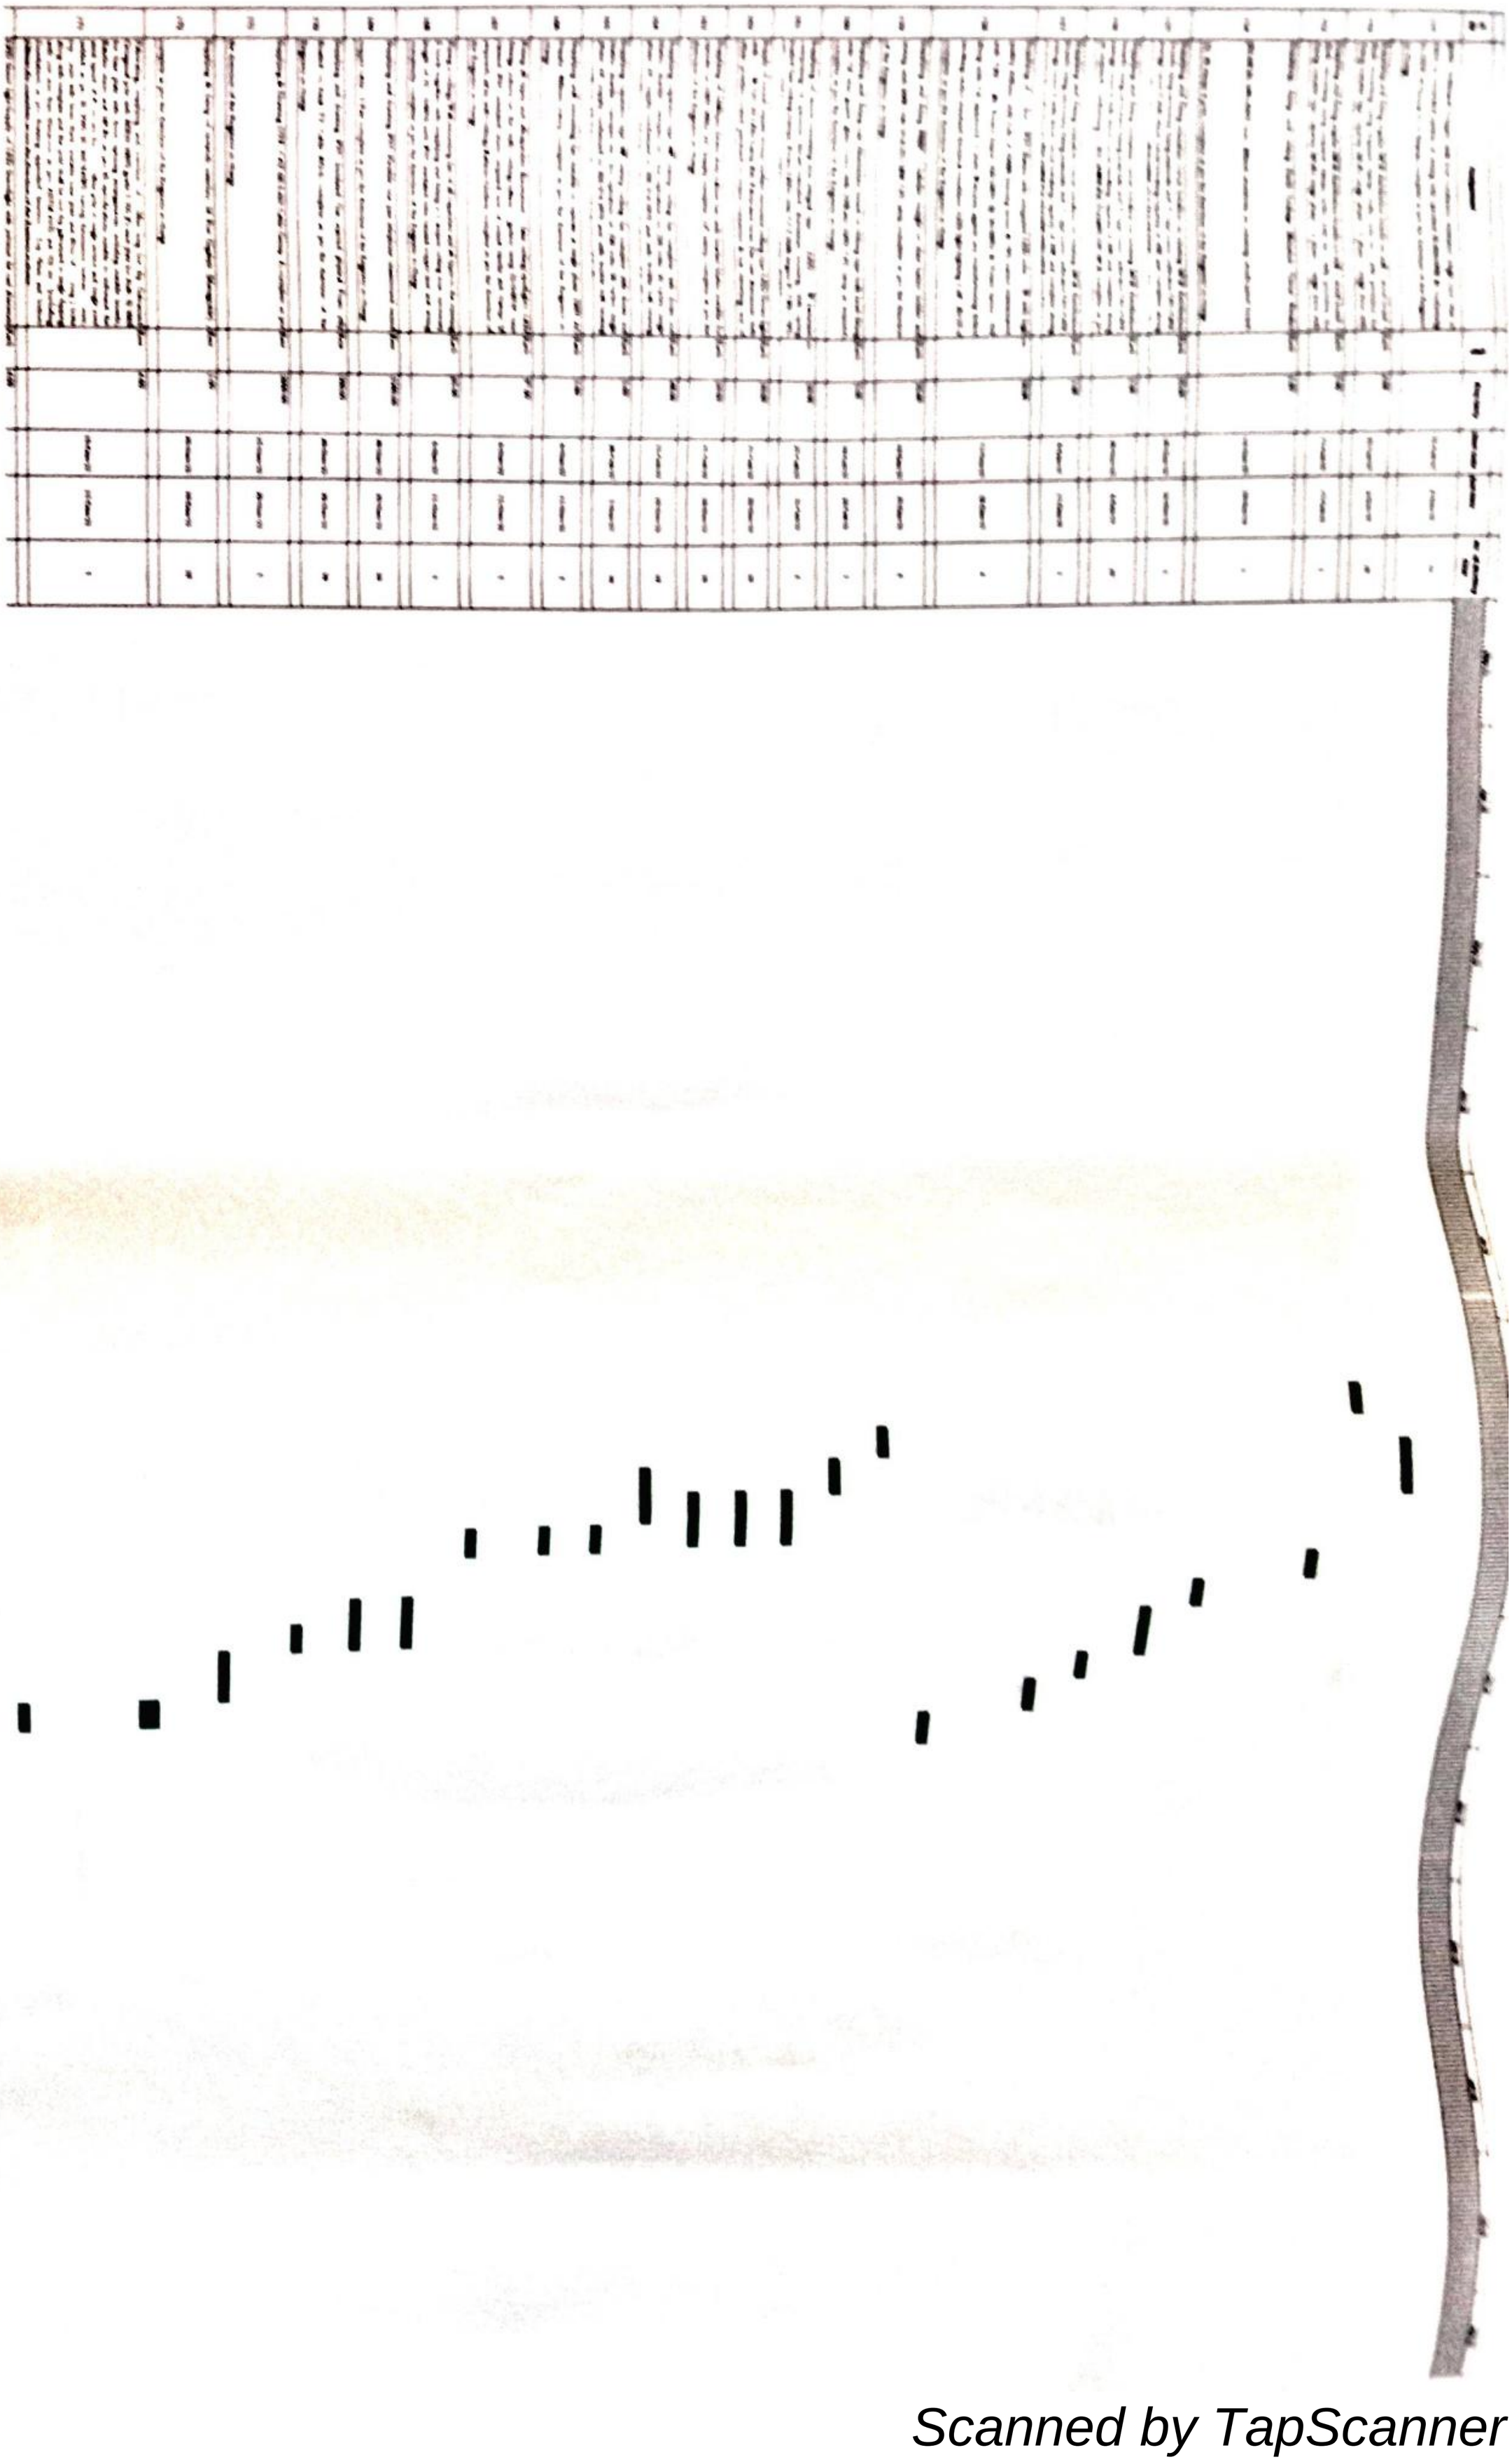

Scanned by TapScanner

Scanned by TapScanner

Sr. No.	Assignment	Unit	Rate/ Cmty	Start Date	End Date	No. of Working Days
184	... 630 ... steel thickness 1.6mm thick ... D: 4270.2001 and ... 1.2 ... 1985 ... 2 ... 1985 ... 4270.2001 ...	...	...	24-Nov-21	30-Nov-21	7
185	... 1.00	...	1.00	24-Nov-21	30-Nov-21	7
186	... 5.00	...	5.00	22-Nov-21	27-Nov-21	5
187	... 1.00	...	1.00	22-Nov-21	27-Nov-21	5
188	... 500.00	Rmt	500.00	23-Nov-21	29-Nov-21	6
189	... 1.00	...	1.00	23-Nov-21	27-Nov-21	5
190	... 2.00	...	2.00	23-Nov-21	27-Nov-21	5
191	... 1.00	...	1.00	22-Nov-21	27-Nov-21	5
192	... 1.00	...	1.00	22-Nov-21	27-Nov-21	5
193	... 1.00	...	1.00	22-Nov-21	27-Nov-21	5
194	... 1.00	...	1.00	30-Nov-21	2-Dec-21	2
195	... 1.00	...	1.00	30-Nov-21	2-Dec-21	2
196	... 5.00	...	5.00	30-Nov-21	2-Dec-21	2
197	... 1.00	Nos	1.00	30-Nov-21	2-Dec-21	2
	...	Mtr	25.00			

Scanned by TapScanner

S. No	Assignment	Unit	Req Qty	Start Date	End Date	No. of Working Days
198	[illegible] galvanised steel wire/steel tape armoured cable with PVC outer sheathing 1.1 KV class 4 core 16 Sqmm PVC cable, complete as per the direction of the Engineer in charge.			30-Nov-21	5-Dec-21	5
199	Labour charges for laying of 1.1 KV Class UG cable 4 Sqmm to 16 sqmm [illegible] complete as per the direction of the Engineer in charge.	Mtr	25.00	30-Nov-21	5-Dec-21	5
200	Digging of trench of [illegible] deep x 0.30 mtr wide refilling the trench to the required ground level and consolidating [illegible] complete as per specifications and direction of the Engineer in Charge.	Mtr	30.00	30-Nov-21	5-Dec-21	5
201	Supplying and fixing Class A (Medium duty) GI pipe [illegible] on pole/wall/Duct [illegible] arrangements for UG Cable of 1.1 KV class [illegible], complete as per the direction of the Engineer in charge.	Mtr	10.00	30-Nov-21	5-Dec-21	5
202	Supplying and fixing LT [illegible] suitable for 1.1 KV class UG cable, filled with [illegible] compound complete. With [illegible] complete for [illegible] Sqmm as per specification, complete as per the direction of the Engineer in charge.	Each	1.00	30-Nov-21	4-Dec-21	4
203	Providing and handling at site work P.V.C Pipe including cost of pipe and specials and labour [illegible] with all labour and lift charges [illegible]	Mtr	75.00	30-Nov-21	2-Dec-21	2
204	Refilling available earth around pipe lines, cables in layers not exceeding [illegible] in depth, [illegible] with all labour complete as per specifications complete as per the direction of the Engineer in charge.	Cum	11.81	30-Nov-21	4-Dec-21	4
205	[illegible] charges & KEB Deposit, complete as per the direction of the Engineer in charge.	Nos	1.00	4-Dec-21	5-Dec-21	1
206	Providing and applying Polymer based water proofing [illegible] Temperature of 200 DegC [illegible] Water Dampness & seepages, comprising of [illegible]	Sqm	43.50	7-Dec-21	17-Dec-21	10
207	Providing and fixing [illegible] including all lead & lift, loading & unloading, cost of materials and other incidental charges etc., complete as per specification and as per the directions by the Engineer in charge of the work complete as per the direction of the Engineer in charge.	Each	1.00	20-Dec-21	30-Dec-21	10
208	[illegible]	Each	5.00	5-Dec-21	15-Dec-21	10
209	Provision of 5 H P (3.7 KW) [illegible] ATLANTA / SUGUNA / CRI / KIRLOSKAR and other equivalent three phase submersible pump [illegible] complete as per the direction of the Engineer in charge.	Each	1.00	15-Dec-21	25-Dec-21	10
210	Providing and fixing M.S. [illegible]	Sqm	60.00	15-Dec-21	20-Dec-21	5
211	Providing and fixing M.S. Gate as per Chief Architect Drawing [illegible]	Sqm	22.50	15-Dec-21	20-Dec-21	5
212	[illegible]	Sqm	84.40	1-Jan-22	11-Jan-22	10
213	Providing and fixing [illegible]	Sqm	9.60	15-Dec-21	25-Dec-21	10
214	Providing and fixing [illegible] (BBMP Approved) Ground Floor complete as per the direction of the Engineer in charge.	Each	96.00	26-Dec-21	31-Dec-21	5
215	Providing and fixing [illegible] (BBMP Approved) First Floor complete as per the direction of the Engineer in charge.	Each	108.00	26-Dec-21	31-Dec-21	5
216	Providing and fixing [illegible] (BBMP Approved) Second Floor complete as per the direction of the Engineer in charge.	Each	120.00	26-Dec-21	31-Dec-21	5
217	Providing and fixing [illegible] (BBMP Approved) Third Floor complete as per the direction of the Engineer in charge.	Each	15.00	1-Jan-22	6-Jan-22	5
	Providing and fixing [illegible]	Nos	1.00			

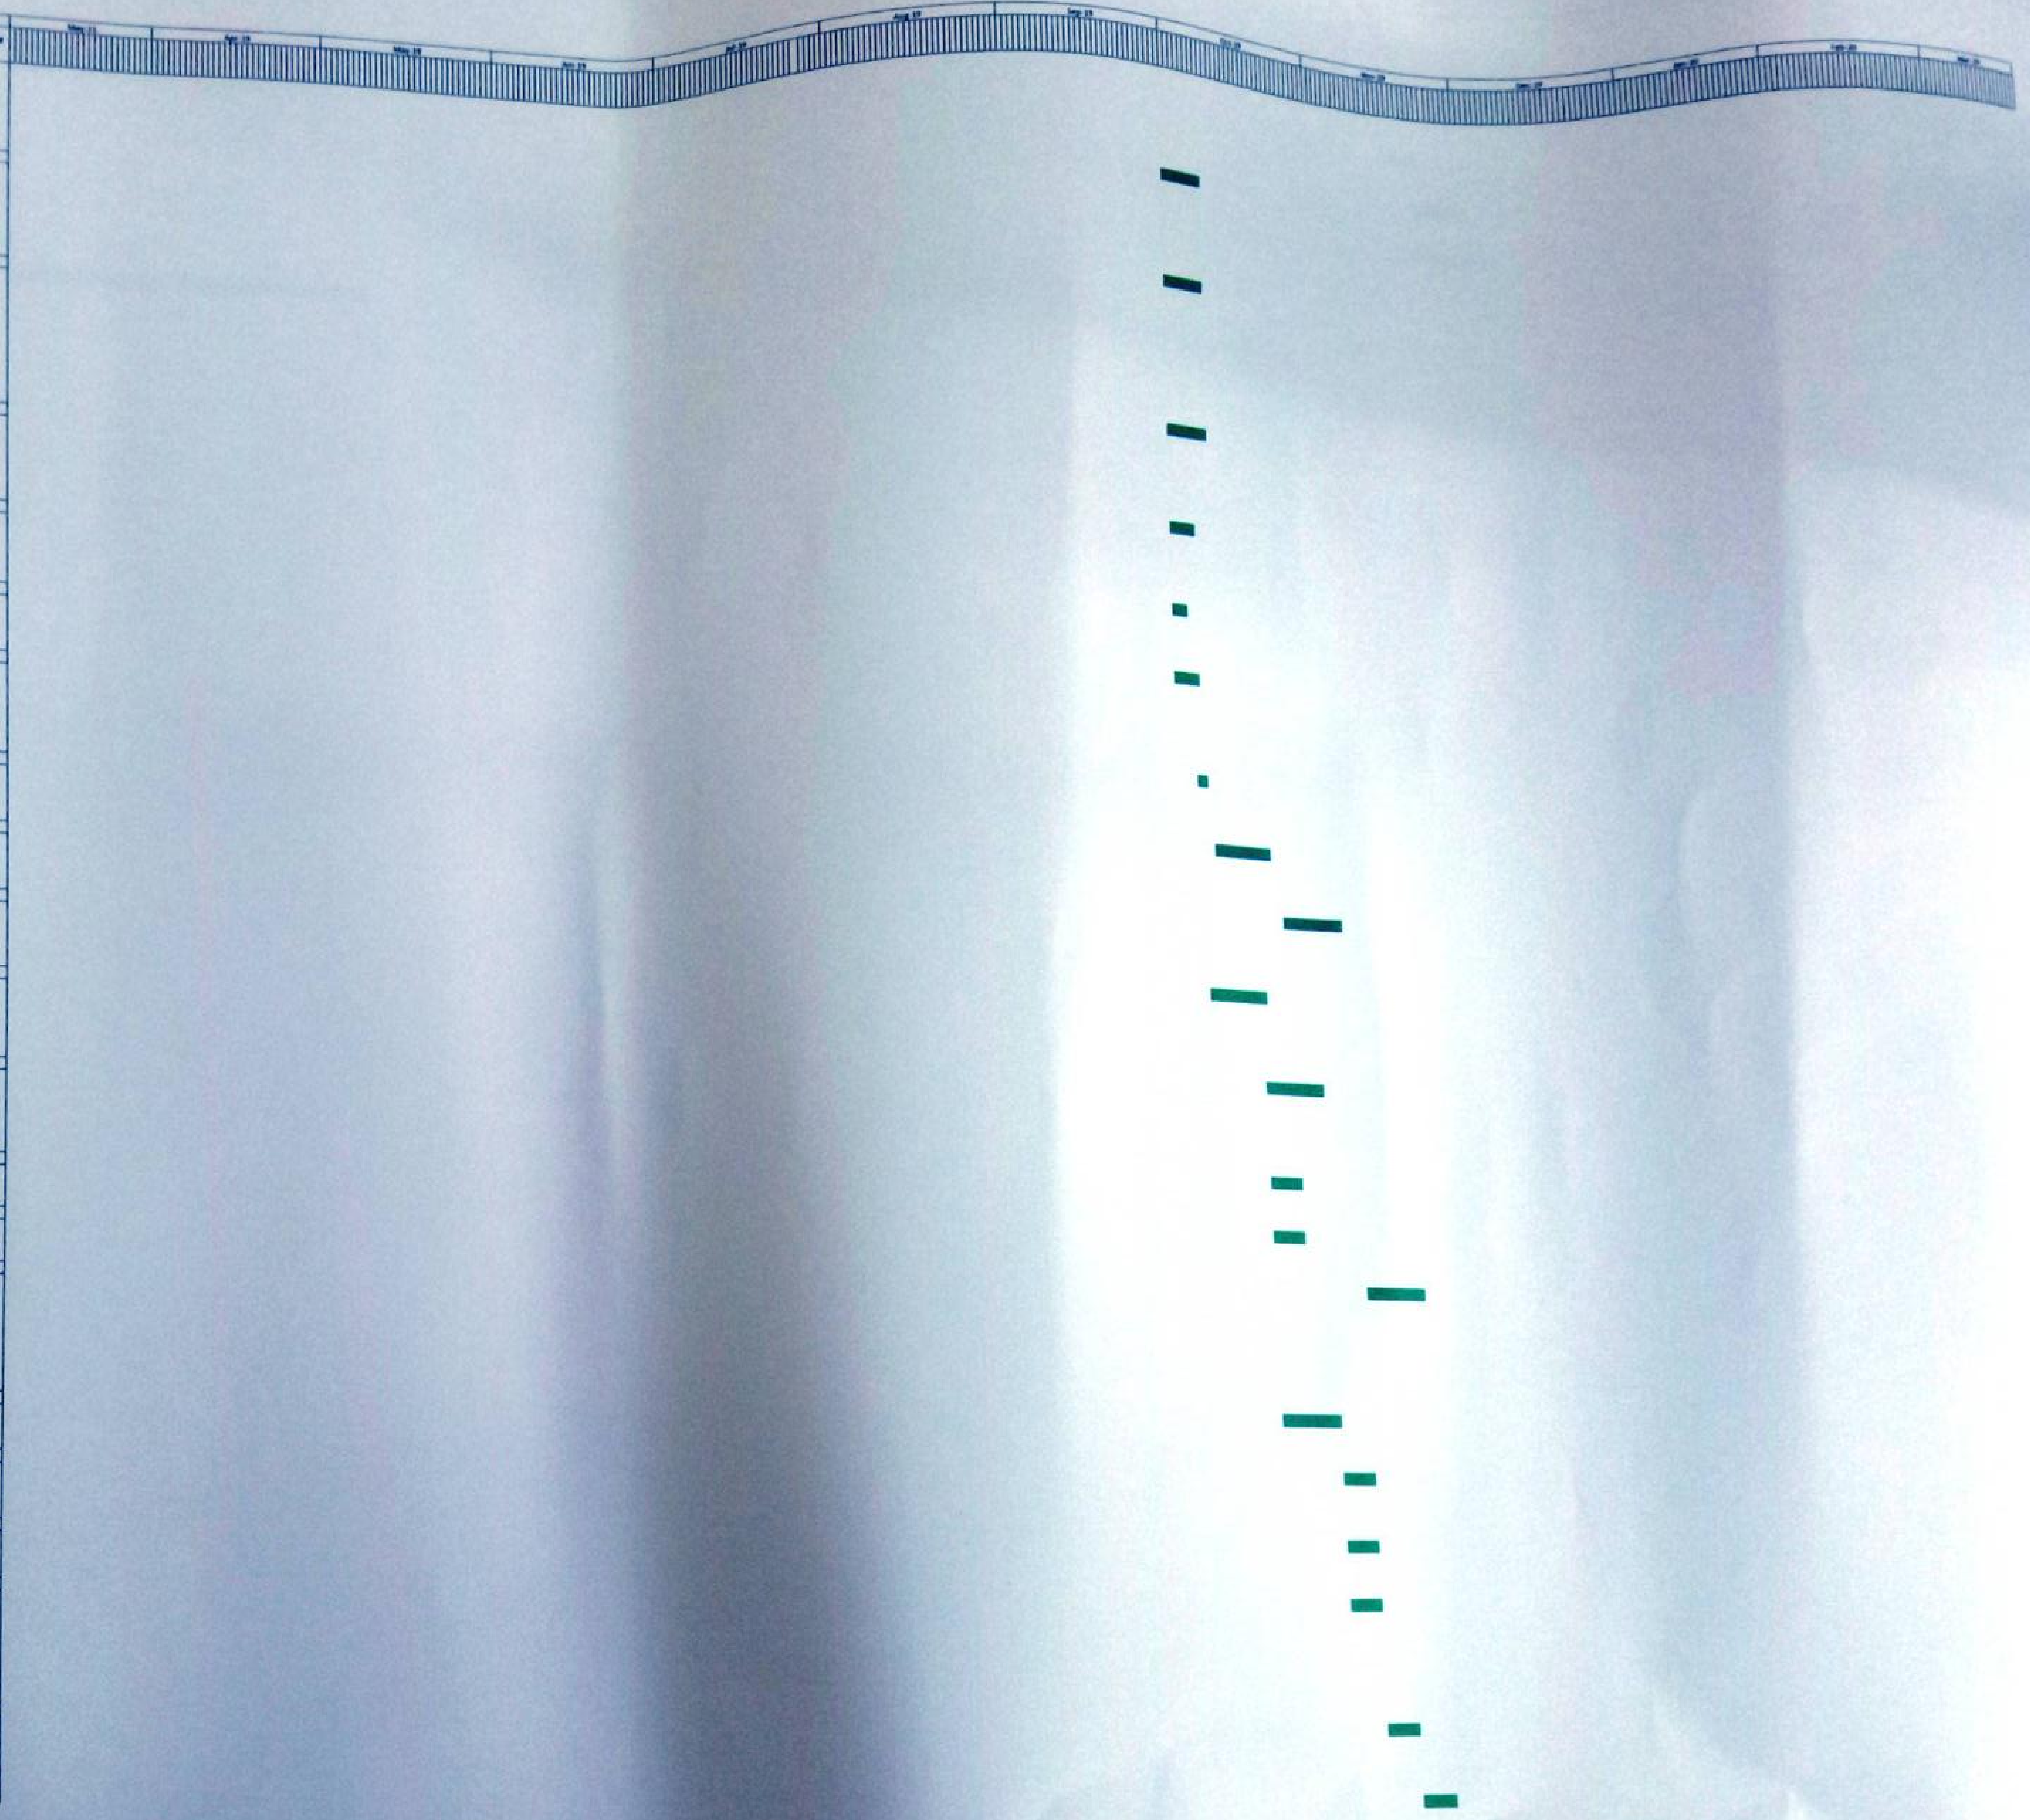

SN	Assignment	Type	Duration	Start Date	End Date	No. of Consulting Days
218	...edge bounded, 25 mm thick PLYW with edge bonded Shelf table,28 mm thick PLYW with edge bonded Modesty, Hardware Module assembly and waste bag...			7-Jun-22	13-Jun-22	5
219	...Consulting and Group Five Standing Table for Cabin without frames consisting of 25 mm thick PLYW table top, 25 mm thick PLYW with edge bonded Shelf table,28 mm thick PLYW with edge bonded Modesty, Wire manager - ABS...	New	5.00	13-Jun-22	18-Jun-22	5
220	...Consulting and Group Five Standing Table for Cabin without frames consisting of 25 mm thick PLYW table top, 25 mm thick PLYW with edge bonded Shelf table,28 mm thick PLYW with edge bonded Modesty, Wire manager - ABS...	New	10.00	18-Jun-22	28-Jun-22	10
221	...Consulting and Group Five Standing Table for Cabin without frames consisting of 25 mm thick PLYW table top, 25 mm thick PLYW with edge bonded Shelf table,28 mm thick PLYW with edge bonded Modesty, Wire manager - ABS...	New	10.00	18-Jun-22	28-Jun-22	10

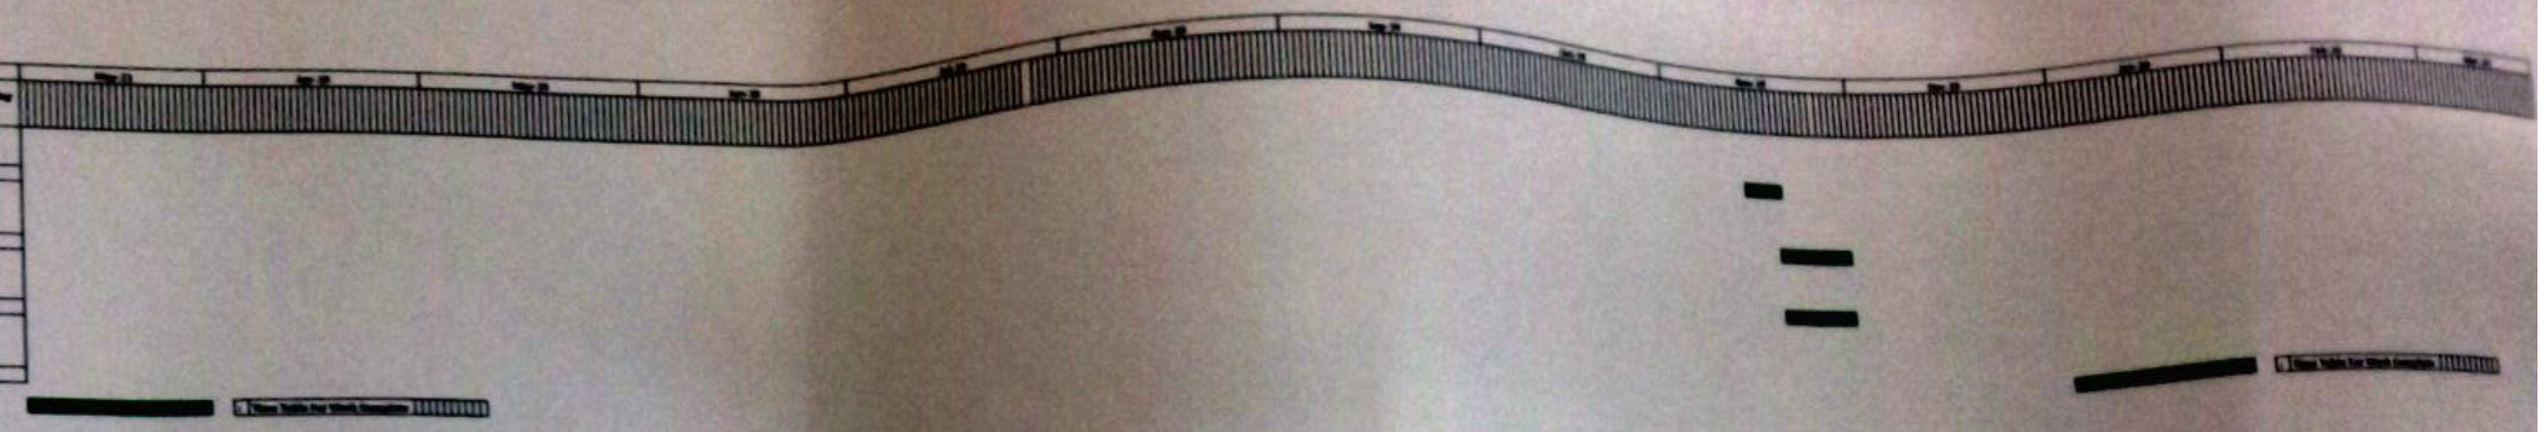

Scanned by TapScanner
